


Draft REV8.0

Activity ID	IPMT Respor	Activity Name	Original Duration	Start	Finish	2017					2018					2019					2020					2021																																																																
						A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																
						4	5	6	7	8	9	1	1	1	1	1	1	1	1	1	1	2	2	2	2	2	2	2	2	2	2	3	3	3	3	3	3	3	3	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	4	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	5	6	6	6	6	6	6	6	6	6	6	6	6	6	6
PH4.5.15935		(LOE) CR Single Track Duration	593	11-Feb-18	27-Sep-19																																																																																					
Bridges			180	12-Feb-18	29-Oct-18																																																																																					
Medford Street Bridge			180	12-Feb-18	29-Oct-18																																																																																					
No IPMT Responsibility			180	12-Feb-18	29-Oct-18																																																																																					
A11680		Interim Design	60	12-Feb-18	08-May-18																																																																																					
A11690		Final Design to IFC	120	09-May-18	29-Oct-18																																																																																					
NEW HAMPSHIRE MAINLINE BRANCH			733	30-Oct-18	29-Sep-21																																																																																					
MEDFORD STREET AREA (275+00 to 240+00) (Gillman)			286	30-Oct-18	19-Dec-19																																																																																					
Medford Street Bridge			286	30-Oct-18	19-Dec-19																																																																																					
No IPMT Responsibility			409	06-Nov-18	19-Dec-19																																																																																					
PH4.5.10085		Medford TLD	409	06-Nov-18	19-Dec-19																																																																																					
Demo & Enabling			49	30-Oct-18	10-Jan-19																																																																																					
No IPMT Responsibility			49	30-Oct-18	10-Jan-19																																																																																					
PH4.5.10075		Establish Traffic Controls & Close Roadway - Medford Street Bridge	5	30-Oct-18	05-Nov-18																																																																																					
PH4.5.10080		Close Medford Street Bridge	0	06-Nov-18																																																																																						
PH4.5.10110		Bridge Demolition - Medford Street Bridge	38	06-Nov-18	10-Jan-19																																																																																					
North Abutment			19	11-Jan-19	14-Feb-19																																																																																					
No IPMT Responsibility			19	11-Jan-19	14-Feb-19																																																																																					
PH4.5.10090		SOE/Exc/FRP North Abutment - Medford Street Bridge	19	11-Jan-19	14-Feb-19																																																																																					
Center Pier			19	14-Feb-19	17-Mar-19																																																																																					
No IPMT Responsibility			19	14-Feb-19	17-Mar-19																																																																																					
PH4.5.10095		SOE/Exc/FRP Center Pier - Medford Street Bridge	19	14-Feb-19	17-Mar-19																																																																																					
South Abutment			42	17-Mar-19	15-May-19																																																																																					
No IPMT Responsibility			42	17-Mar-19	15-May-19																																																																																					
PH4.5.10100		SOE/Exc South Abutment - Medford Street Bridge	19	17-Mar-19	06-Apr-19																																																																																					
PH4.5.10145		Construct Mud Mat & Footings - South Abutment Medford Street Bridge	7	08-Apr-19	17-Apr-19																																																																																					
PH4.5.10150		Construct South Abutments - Medford Street Bridge	20	18-Apr-19	15-May-19																																																																																					
Superstructure			112	16-May-19	24-Oct-19																																																																																					
No IPMT Responsibility			112	16-May-19	24-Oct-19																																																																																					
PH4.5.10165		Construct South Side Wing Walls - Medford Street Bridge	15	16-May-19	06-Jun-19																																																																																					
PH4.5.10170		Construct Deck - Medford Street Bridge	95	07-Jun-19	22-Oct-19																																																																																					
PH4.5.10175		Construct E & W Approach Slabs - Medford Street Bridge	2	23-Oct-19	24-Oct-19																																																																																					
Civil Work/Traffic Improvements			40	23-Oct-19	19-Dec-19																																																																																					
No IPMT Responsibility			40	23-Oct-19	19-Dec-19																																																																																					
PH4.5.10185		Civil Work/Traffic Improvements (Medford Street)	40	23-Oct-19	19-Dec-19																																																																																					
LOWELL ST AREA (314.00 to 275.00)			504	27-Sep-19	29-Sep-21																																																																																					
School Street Bridge (274.50)			504	27-Sep-19	29-Sep-21																																																																																					
Bridge			504	27-Sep-19	29-Sep-21																																																																																					
No IPMT Responsibility			504	27-Sep-19	29-Sep-21																																																																																					
PH4.5.15435		School St Bridge TLD	734	27-Sep-19	29-Sep-21																																																																																					
PH4.5.10805		Open Medford Street and Close School Street	5	20-Dec-19	27-Dec-19																																																																																					
PH4.5.11675		Bridge Demolition - School Street Bridge	14	30-Dec-19	24-Jan-20																																																																																					

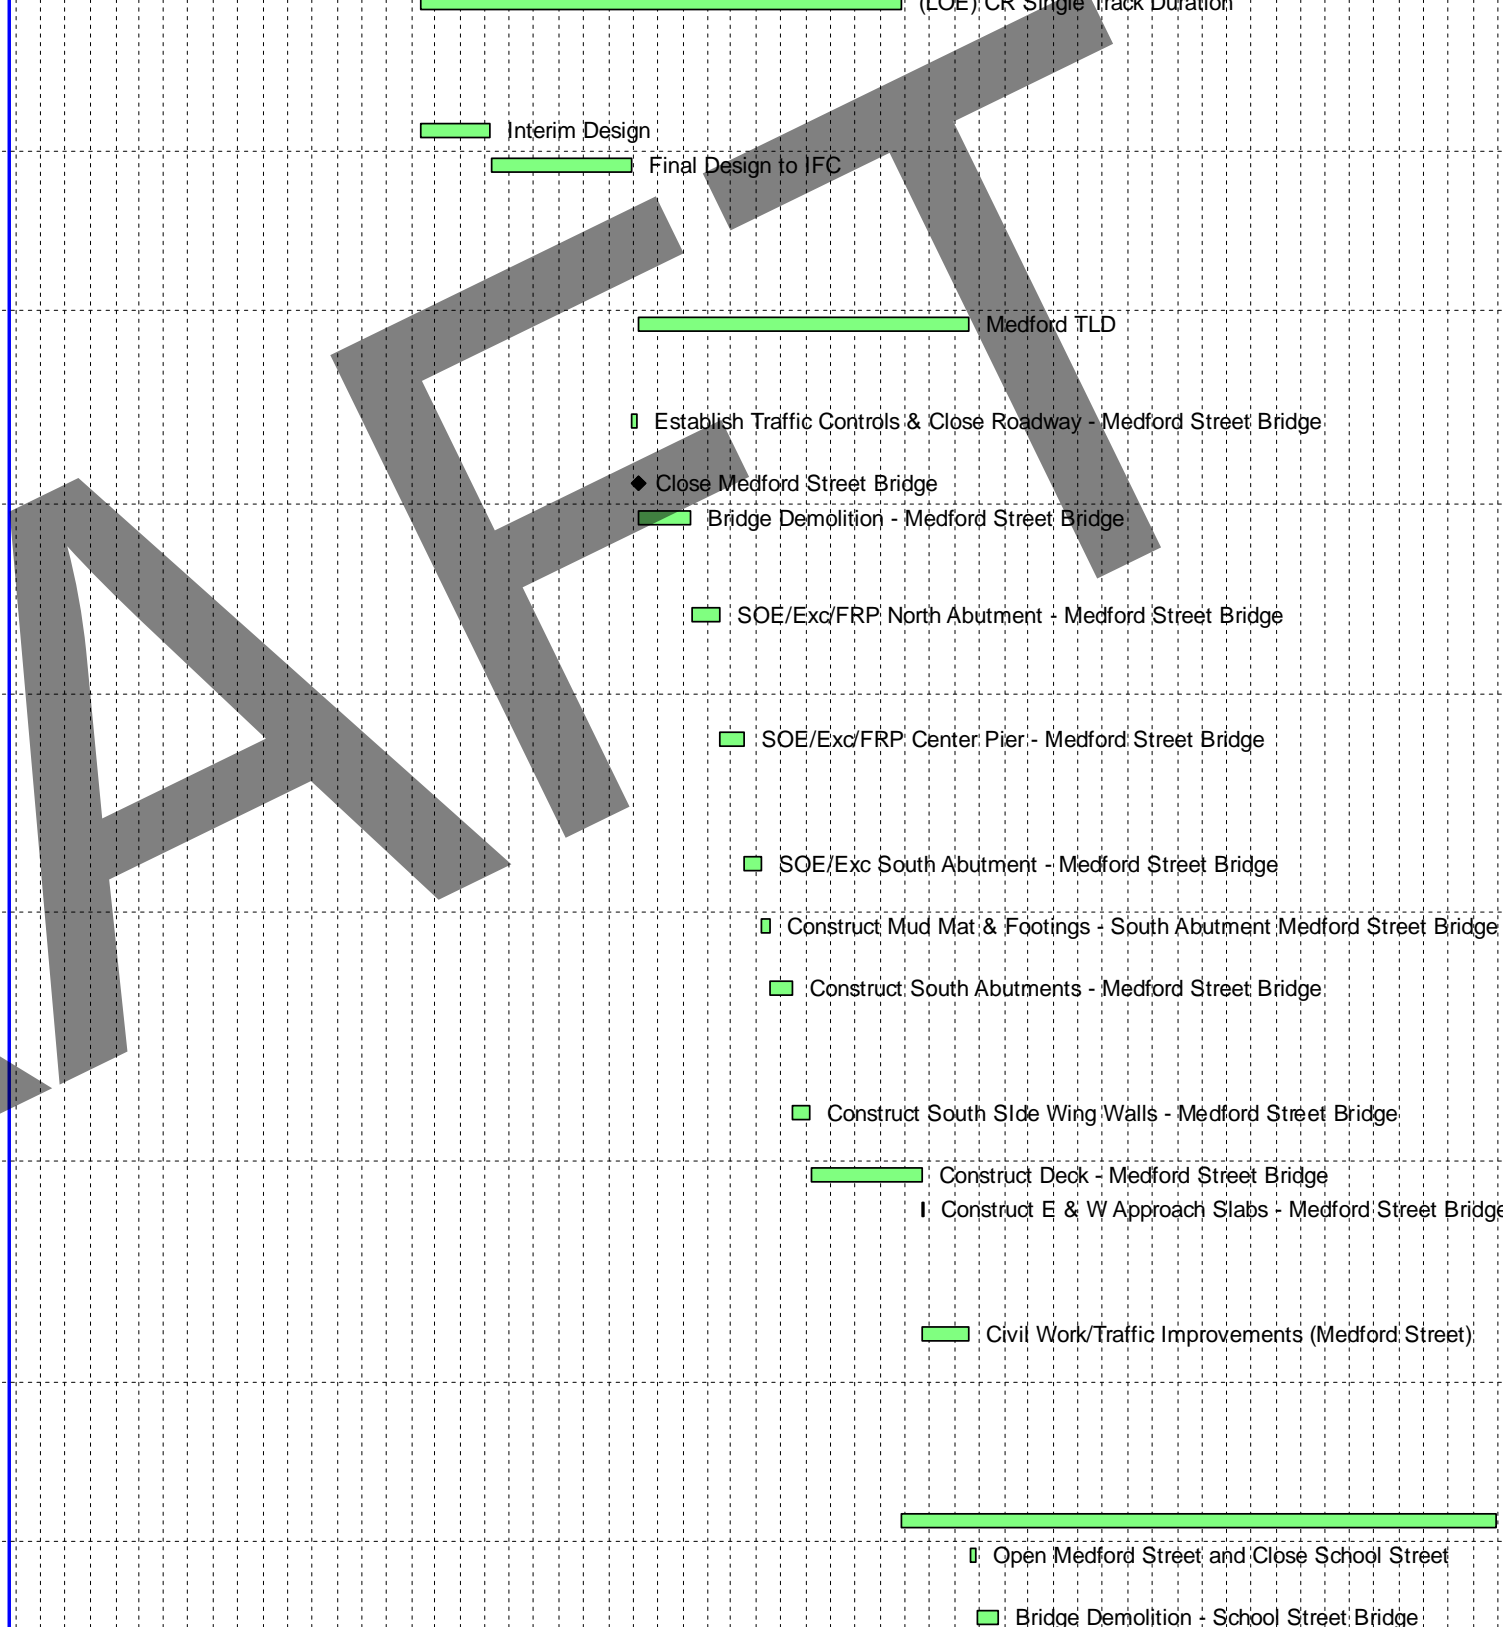

Activity ID	IPMT Respor	Activity Name	Original Duration	Start	Finish	2017																																																				2018																																																				2019																																																				2020																																																				2021																																																			
						2017					2018					2019					2020					2021																																																																																																																																																																																																																																															
						A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D																																																																																																																																																																																																			
PH4.5.11680		Install SOE & Excavate to Grade - School Street Bridge	19	24-Jan-20	02-Mar-20																																																																																																																																																																																																																																																																				
PH4.5.11685		Construct Mud Mat & Footings - School Street Bridge	4	02-Mar-20	06-Mar-20																																																																																																																																																																																																																																																																				
PH4.5.10740		Construct Abutments - School Street Bridge	26	06-Mar-20	29-Mar-20																																																																																																																																																																																																																																																																				
PH4.5.10785		Construct Wing Walls - School Street Bridge	24	30-Mar-20	01-May-20																																																																																																																																																																																																																																																																				
PH4.5.10790		Construct Deck - School Street Bridge	46	04-May-20	08-Jul-20																																																																																																																																																																																																																																																																				
PH4.5.SB2100		Run Permanent Electrical Duct Across School Street Bridge	10	09-Jul-20	22-Jul-20																																																																																																																																																																																																																																																																				
PH4.5.UB1700		NSTAR - Pull Cable Cut Over To Permanent - School St Bridge	126	01-Sep-20	13-May-21																																																																																																																																																																																																																																																																				
PH4.5.UB1710		NSTAR - Remove Electrical and Telephone/Temporary Conduit - School St Bridge	6	14-May-21	21-May-21																																																																																																																																																																																																																																																																				
PH4.5.MS		Complete School Street Bridge (Verizon Cut-Over) - Not Required for Revenue Service	0		29-Sep-21																																																																																																																																																																																																																																																																				
Civil Work/Traffic Improvements			90	24-May-21	29-Sep-21																																																																																																																																																																																																																																																																				
No IPMT Responsibility			90	24-May-21	29-Sep-21																																																																																																																																																																																																																																																																				
PH4.5.10810		School Steet Civil Work/Traffic Improvements (School Street)	90	24-May-21	29-Sep-21																																																																																																																																																																																																																																																																				

DRAFT
